

Pump Station #15 Service Area, Phase I, First View Avenue, Sanitary Sewer and Water Upgrades (West Ocean View, Northside)


Project Manager:
Kevin Frederick (757) 664-6734

Consultant:
O'Brien & Gere (757) 431-2966

Construction Inspector: N/A

Supervisor: N/A

Project Scope: Evaluation, design and construction of replacement and rehabilitation of existing water and sanitary sewer lines.

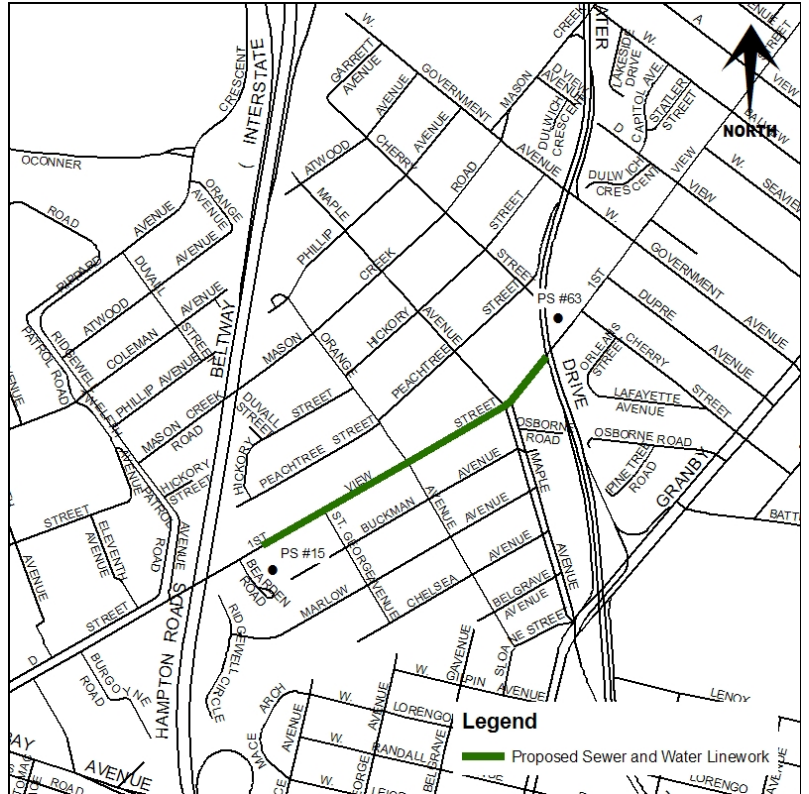

PROJECT STATUS

PRELIMINARY ENGINEERING
(SERVICE AREA): 100% Complete
(Completed January 2009)

PHASE I DESIGN: 65% Complete

Funding Information

Project Budget: Approximately \$92,000

Project Schedule

Design Schedule: Estimated Completion Spring 2010

Construction Schedule: Estimated Start Summer 2010
Estimated Completion Summer 2011

CONTRACT:

Advertised: N/A

Awarded: N/A

Contractor: N/A

COMMUNITY CONNECTION:

Civic Leagues: West Ocean View; Northside

Wards: 1, 5

NOTES: 65% Design Submittal has been forwarded to City for review.
