

11/18/2009

Pump Station 97 Rehabilitation

Project Manager: Don Ewell 757-664-6724
Leticia Quejada 757-664-6768

Construction Inspector: Gary Kimber,
757-823-1104

Supervisor: Ken Schwarz 757-823-1038

Consultant: Greeley and Hansen

Project Scope: Rehabilitation of the pump station #97
wet well.

PROJECT BUDGET:

Design Budget: \$67,421.00

Construction Project Budget: TBD

PROJECT STATUS:

Planning: 100% Complete

Design: 90% Complete

Construction: 0% Completed

PROJECT SCHEDULE:

Design: Completed Fall 2009


Construction: Estimated Start Summer 2010
Estimated completion Summer 2010

COMMUNITY CONNECTION

Civic League(s): Downtown

Ward: 2

Notes: Design is currently underway to rehabilitate the wet well to Pump Station #97, which is in the basement of the Norfolk Scope.

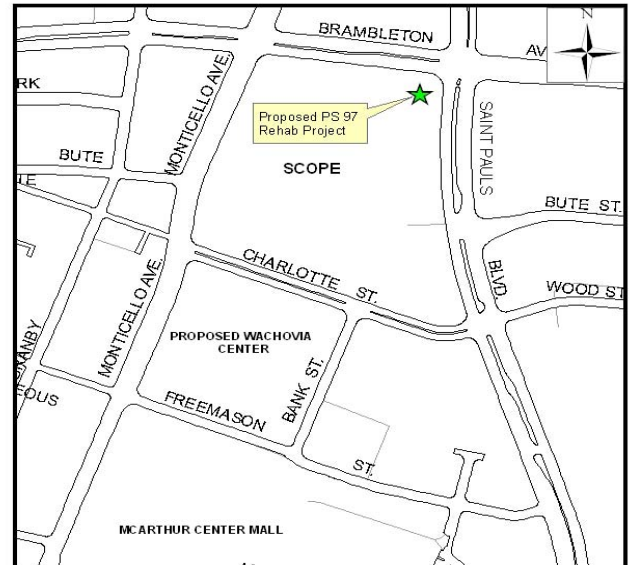

PROJECT LOCATION MAP
