

WEST OCEAN VIEW/NORTHSIDE WATER AND SANITARY SEWER REPLACEMENT – PHASE 2

Project Manager:

Kevin Frederick, 664-6734

Consultant:

O'Brien & Gere, 431-2966

Construction Inspector:

TBA

Supervisor:


TBA

Project Scope: Evaluation, design and construction to replace and rehabilitate the existing water and sanitary sewer lines.

Project Status:

Preliminary Engineering (Service Area):
100% Complete (Completed January 2009)

Phase 2 Design: 95% Complete

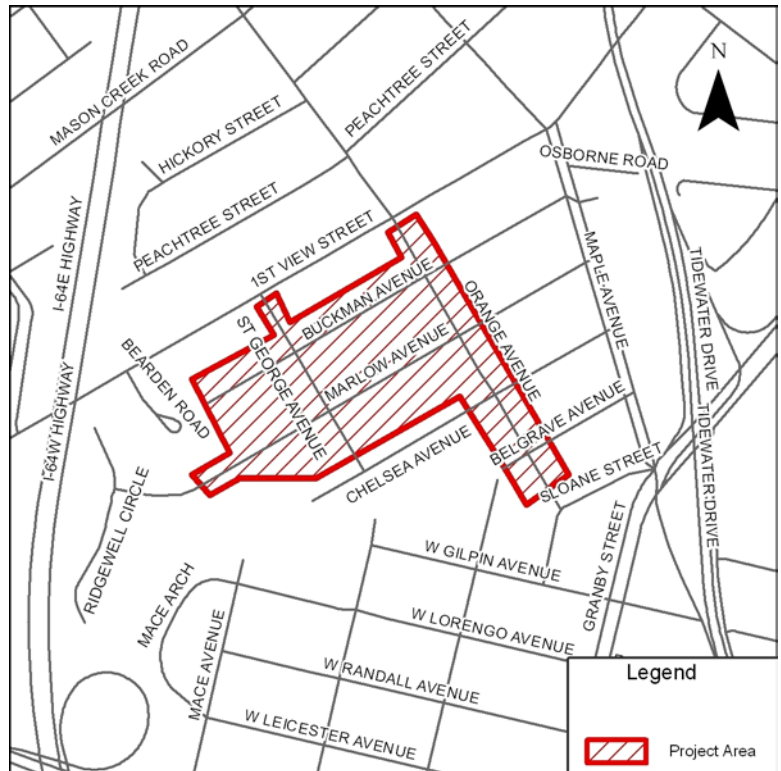

Project Budget: Approximately \$226,200 (Design)

Project Schedule

Design Schedule: Estimated Completion Spring 2012

Construction Schedule: Estimated Start Summer 2012
Estimated Completion Winter (1st Quarter) 2014

Contract:

Advertised: N/A

Awarded: N/A

Contractor: N/A

Community Connection:

Wards: 1&5

Civic Leagues: Ocean View; Northside

Notes: Design progress towards 100% Design by Engineer Consultant continues.
