

CHESTERFIELD HEIGHTS WATER AND SEWER REPLACEMENT (3 ANNUAL CONSTRUCTION CONTRACTS) – OHIO CREEK WATERSHED

Construct new sanitary sewer mains and new water mains along Westminster Ave., Victoria Ave., Stanhope Ave., Kimball Terrace, and Chesterfield Blvd.

COMMUNITY CONNECTION

Ward / Superward: 4 / 7

Civic League: Chesterfield Heights

Civic League Meetings: 09/23/19 Last Meeting
11/18/19 Next Meeting

Project Bulletins: 02/06/19 Construction Start/Finish

PROJECT STATUS

	<u>Design</u>	<u>Construction</u>
Budget:		\$7,000,000
Contract Amount:	\$240,080	TA Sheets: \$3,330,075 TUC: \$3,275,423 Inner-View: \$1,110,865
Start:	Dec. 2019	March 2019 (sewer) March 2019 (water)
% Complete:	100%	50%
Finish:	Feb 2019	Spring 2022


PROJECT TEAM

Project Manager: Rick Dempsey

Const. Inspector: Jamal Dean, Alex Swafford

Consultant: Arcadis

Contractor: TA Sheets, Tidewater Utility, Inner-View

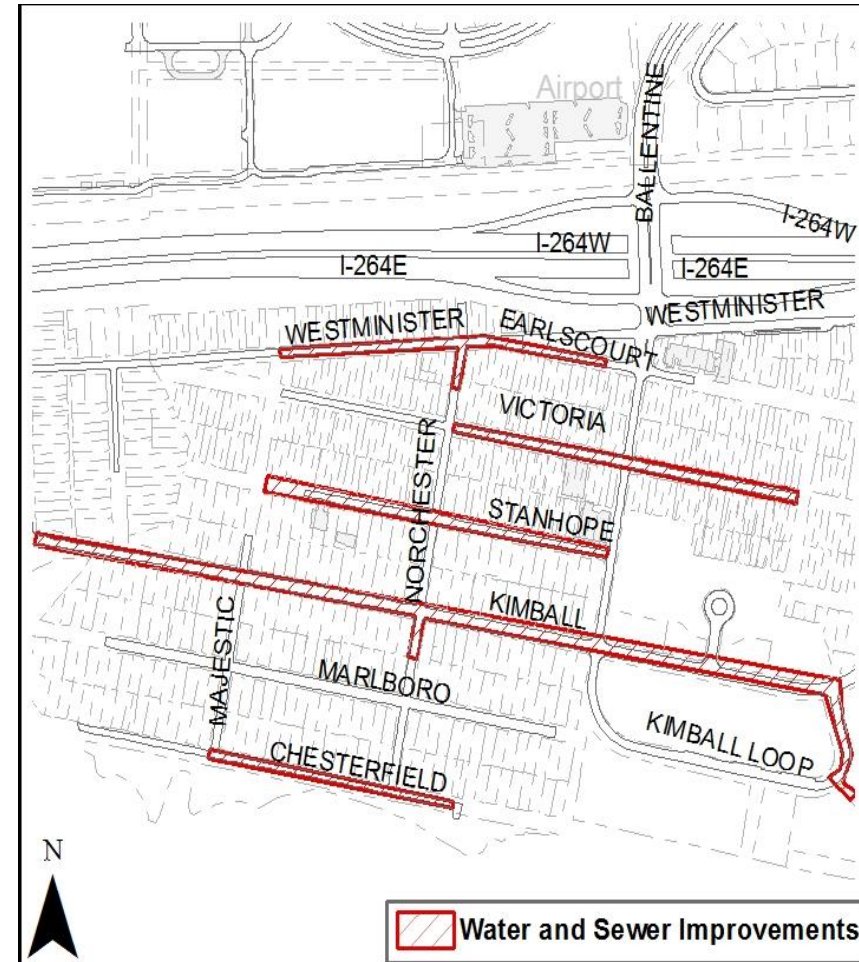

NOTES: HRSD Cost Sharing: \$1,500,000; Norfolk Resilience Office: \$500,000 (*TBD*)
