

RAW WATER LINE #3 RELOCATION TO SUPPORT CWRY EXPANSION

Route study, design, and construction of 9,020 LF of 48in raw water main and 9,000 LF of 30in finished water main.

COMMUNITY CONNECTION


Ward / Superward: N/A
 Civic League: City of Suffolk
 Civic League Meetings: N/A
 Project Bulletins: Survey 4/7/21
 Const. Start / Finish: TBD

PROJECT STATUS

	<u>Design</u>	<u>Construction</u>
Budget:	\$1,338,940	\$19,512,119
Contract Amount:	\$1,338,940	TBD
Start:	Summer 2021	Spring 2024
% Complete:	85%	0%
Finish:	Fall 2023	Fall/Winter 2025

PROJECT TEAM

Project Manager: Dan Riley
 Const. Inspector: TBD
 Consultant: Michael Baker
 Contractor: TBD

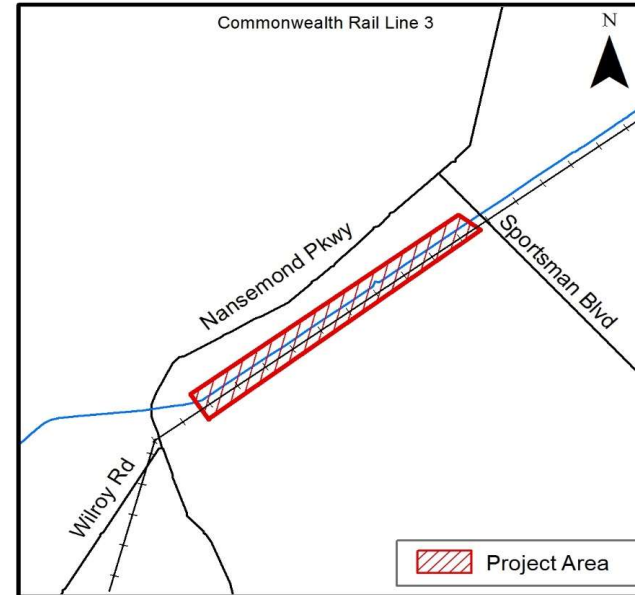

NOTES

Project includes Route Study, Property Acquisition, Grant Agreement with State, and Cost Share Agreement with Portsmouth. Negotiations concluded on sub-grant with VPA and Cost Share Agreement with Portsmouth; ordinances approved by Council.
