

## RIVER FOREST SHORES PUMP STATION #93 REHABILITATION

### COMMUNITY CONNECTION


Ward/Superward: 4/7  
 Civic League: River Forest  
 Meeting Recurrence: 1<sup>st</sup> Monday monthly (Sept. – June)  
 Last Meeting: October 10<sup>th</sup>  
 Next Meeting: November 7<sup>th</sup>  
 Bulletin: Construction 6/30/22 – A new one TBA

### PROJECT STATUS

<u>Construction Phase</u>	<u>Original</u>	<u>Adjusted</u>
Budget:	\$2.5M	NA
Contract Amount:	\$1,492,170	NA
Start:	Summer 2022	Winter 2023
% Complete:	0%	NA
Finish:	Winter 2023	Summer 2023

### PROJECT TEAM

Project Manager: Mandy Kuhr  
 Consultant: Arcadis  
 Contractor: SHAW  
 Note: Self-imposed goal completion date for performance evaluation TBA.

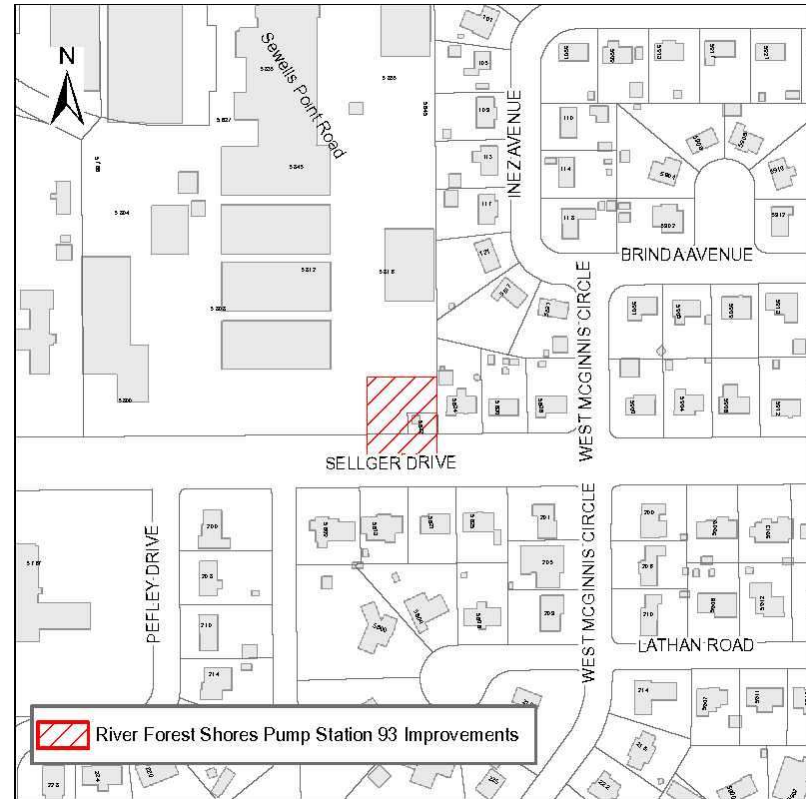

### NOTES

Waiting for the property acquisition process to complete. Construction start has been delayed. Change order requested for work done so far and stored materials. Cost impact may roll over to renting a bypass pump and if construction starts in the winter may have weather delays.
