

RIVER OAKS/FOX HALL PUMP STATION # 44 SERVICE AREA PHASE 2 WATER AND SEWER REPLACEMENT

VRA & EPA Funding

Installation of approximately 2,100 LF of gravity sanitary sewer, approximately 1,800 LF of water mains.

COMMUNITY CONNECTION


Ward / Superward: 4 / 7
Civic League: River Oaks/Fox Hall
Civic League Meetings: 9/13/2022
Project Bulletins: 2/2/22 (Construction)

PROJECT STATUS

	<u>Design</u>	<u>Construction</u>
Budget:	\$150,000	\$3,170,000
Contract Amount:	\$159,545	\$2,887,813
Start:	Summer 2020	Spring 2022
% Complete:	100%	75%
Finish:	Spring 2021	Spring 2024

PROJECT TEAM

Project Manager: Dan Riley
Const. Inspector: Charles Davis
Consultant: Bamforth
Contractor: Tidewater Construction

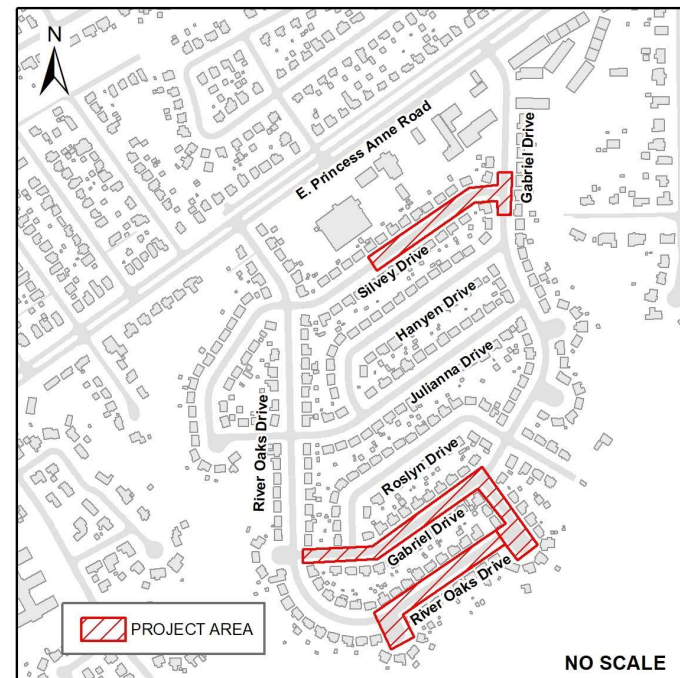

Project Area
